



# CITYheart.

# update

project update information

week of 19 January 2009

## making progress




### WORK COMPLETED THIS WEEK:

- We have now completed the ducting along the entire western side of Victoria Street and from ArtsPost to just short of the Embassy site reserve on the eastern side. This ducting is needed to carry power supply and other cables (e.g. for lighting)
- We have formed the new kerb and channel on the eastern side from ArtsPost to Marlborough Place and prepared the ground for forming the new kerb from Marlborough Place up to the "Devilish" premises
- Drainage: we have laid connections from building down pipes to back of kerbs on the eastern side
- The old kerb has been removed from the Le Grand corner to the new speed table (by Burger Fuel)
- The ground has been dug out and prepared for the new speed table at the Embassy site reserve.



### PLANNED WORK FOR NEXT WEEK:

- New temporary traffic management will be in operation from Collingwood Street traffic signals southwards – see attached drawing (all affected parties have been notified)
- Form the new kerb and channel from Marlborough Place up to the "Devilish" premises
- Form the new kerb and channel from Le Grand to Lone Star
- Install kerb outlet units in the new kerbs (these will discharge the water from building down pipes)
- Construct the concrete approach beams and top slab for the new speed table at Embassy site reserve
- Pour exposed aggregate paving panels behind the new kerb outside Furnace
- Backfill and complete behind all the new sections of kerb and channel.

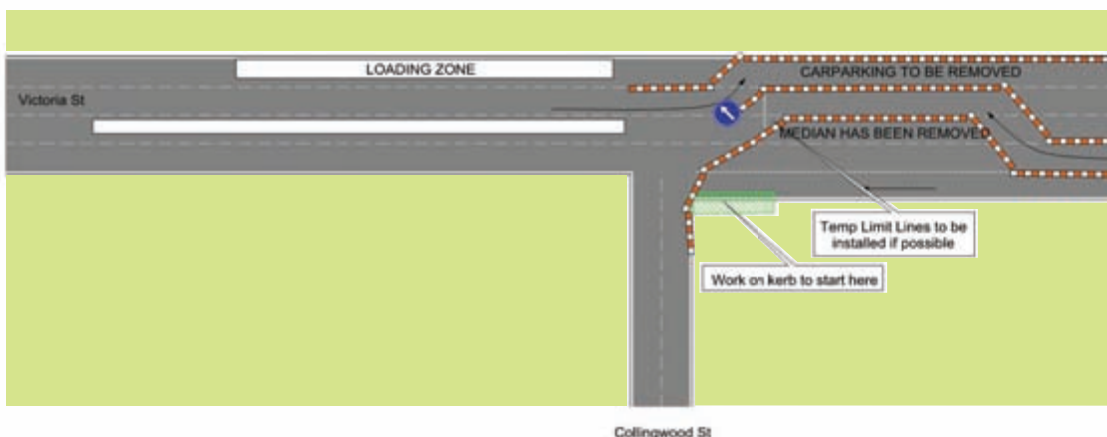

## weekly meetings

**THIS WEEK** Come along to Metropolis Caffe at 211 Victoria Street  
**WHEN** Wednesday 21 January 09, 10.30am

